


---

## Butler SD Renovation Projects Phase II Summer of 2023 Weekly Progress Report Status April 29, 2023, through May 05, 2023

---

This week at Brook Forest, we completed the roofing on the addition of Brook Forest. This included HVAC roof curbs, existing opening infills, and plumbing vents. We also completed the interior wall stud framing. The next stages include plumbing, electrical, and HVAC rough-ins for the addition. Masonry veneer will also start in the next couple of weeks. We are planning and coordinating all required activities once school is out for summer vacation.

This project is currently on schedule.

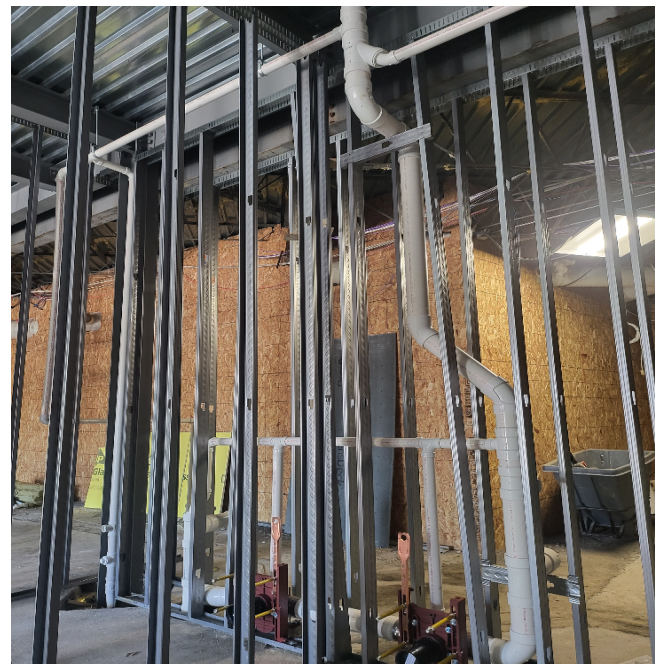

This week at Butler Junior High, the masons mobilized and began to lay blocks on the addition. This process should take approximately 6 – 7 days and will be followed by waterproofing applied to the exterior walls. We are also coordinating and planning work once summer vacation hits. All materials have been ordered with confirmed delivery dates.

The work at Butler Junior High is also currently on schedule.

